





# PROJECT SUMMARY REPORT

January 2018



## AT A GLANCE

- 6 levels
- 2,000 spaces
- First floor to be a **Ground Transportation Center** for commercial vehicles
- Parking Space **Guidance System**
- Capacity for **20,000 gallons of rain water** harvesting for landscape irrigation
- Green-screen **vegetation wall**
- Traffic circulation and terminal access
- Opening **Aug. 31, 2018**

## PROJECT BUDGET <sup>1</sup>

- \$122 million

## PROGRESS <sup>2</sup>

- % of Concrete Placed, To Date: 44.7%
- Weight of Concrete Placed, To Date: 67 million pounds
- Weight Equivalent of Concrete Placed, To Date: 134 Boeing 787 Aircraft
- Total Weight of Concrete, Upon Completion: 150 million pounds
- Total Weight Equivalent of Concrete, Upon Completion: 300 Boeing 787 Aircraft

## SMWBE PARTICIPATION <sup>3</sup>


	GOAL	ACHIEVED
MBE PARTICIPATION	8.33%	1.12%
WBE PARTICIPATION	3.83%	2.31%

## WORK FORCE <sup>4</sup>

- # of Workers: 135 per day
- Regional Labor: 51%
- Total Hours Worked: 101,740

## WORK FORCE BY COUNTY

- OTHER
- DAVIDSON
- COFFEE
- SUMNER
- RUTHERFORD
- WARREN

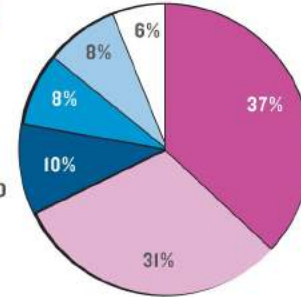

## MATERIALS <sup>5</sup>

- % Regional Materials: 39%

**44.7%**

Quantity of Concrete Placed by Weight

Boeing 787 = 102,900lbs  
1 CY Concrete = 4,050lbs  
27,000 CY Concrete in Parking Garage  
267 Boeing 787's by Weight

**JEDUNI** Metropolitan Nashville Airport Authority

<sup>1</sup> As of 1/17/2018

<sup>2</sup> As of 1/11/2018

<sup>3</sup> As of 12/28/2017

<sup>4</sup> As of 12/4/2017

<sup>5</sup> As of 12/4/2017
