



PROJECT SUMMARY REPORT

April 2018



AT A GLANCE

- 6 levels
- 2,200 spaces
- First floor to be a **Ground Transportation Center** for commercial vehicles
- Parking Space **Guidance System**
- Capacity for 20,000 gallons of rain water harvesting for landscape irrigation
- Green-screen **vegetation wall**
- Traffic circulation and terminal access
- Opening **Fall 2018**

TOTAL PROJECT BUDGET

- \$122 million

PROGRESS ¹

- % of Concrete Placed, To Date: **72.3%**
- Weight of Concrete Placed, To Date: **109 million pounds**
- Weight Equivalent of Concrete Placed, To Date: **217 Boeing 787 Aircraft**
- Total Weight of Concrete, Upon Completion: **150 million pounds**
- Total Weight Equivalent of Concrete, Upon Completion: **300 Boeing 787 Aircraft**

SMWBE PARTICIPATION ²

DESIGN	GOAL	ACHIEVED
MBE PARTICIPATION	6.07%	6.80%
WBE PARTICIPATION	6.74%	5.84%


CONSTRUCTION	GOAL	ACHIEVED
MBE PARTICIPATION	8.33%	1.48%
WBE PARTICIPATION	3.83%	3.18%
SBE PARTICIPATION	-	0.09%

WORK FORCE ³

- Total # of Workers: **608** (averaging **130** on-site per day)
- Regional Labor: **49%**
- Total Hours Worked: **221,588**

WORK FORCE BY COUNTY

- OTHER
- DAVIDSON
- SUMNER
- COFFEE
- WILSON
- RUTHERFORD

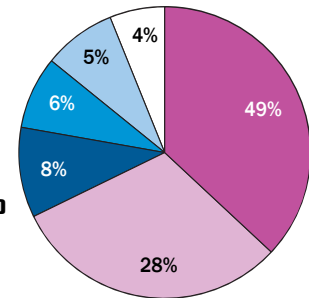

MATERIALS ⁴

- % Regional Materials Used: **36%**

¹ As of 4/12/2018

² As of 4/11/2018

³ As of 2/28/2018

⁴ As of 2/28/2018

72.3%

Quantity of Concrete Placed by Weight

Boeing 787 = 902,500lbs
1 CY Concrete = 4,000lbs
37,500 CY Concrete in Parking Garage
300 Boeing 787's by Weight

JEDUNN
CONCRETE PRODUCTS

Metropolitan Nashville
Airport Authority
