

## Terminal Garage, Pedestrian Plaza and Airport Administrative Building



West elevation of the Terminal Garage, as seen from the Main Terminal. (conceptual image)



Roof canopy under construction over the double-helix ramp system that provides access to parking levels.



# Progress Summary Report

December 2019



Pictured: West elevation of the Terminal Garage, as seen from the Main Terminal.



Aerial view of the Terminal Garage construction site, east elevation.

## At A Glance

- 6 levels of parking:
  - Five levels of public parking (2,800 spaces)
  - New Valet parking area on ground level
- Parking space guidance system
- Electric vehicle charging stations
- 50,000-gallon rainwater harvesting cistern for landscape irrigation
- Pedestrian Plaza
- 64,000-square-foot Airport Administrative Building
- Sustainability: Pursuing **Parksmart** and **LEED** certifications
- Project timeline:
  - Garage will open **Spring 2020**
  - Airport Administrative Building and Pedestrian Plaza will open **February 2021**

- Design-build team: **Messer Construction** and **Moody-Nolan Architects**

## Total Project Budget

- \$183 million

## Progress<sup>1</sup>

- % concrete placed: **82%**
- Total weight of concrete placed: **182 million pounds**
- Total weight of concrete to be placed, by project completion: **223 million pounds**
- Total pieces of steel erected: **2,053**
- Total weight of steel: **1.1 million pounds**

## SMWBE Participation<sup>2</sup>

	GOAL	ACHIEVED
<b>MBE PARTICIPATION</b>	<b>8.69%</b>	<b>3.55%</b>
<b>WBE PARTICIPATION</b>	<b>12.62%</b>	<b>6.21%</b>
<b>SBE PARTICIPATION</b>	<b>4.00%</b>	<b>0.88%</b>


- Paid to Date: **\$18.4 million**

## Work Force<sup>3</sup>

- Total # of workers: **1,045**
- Average # of workers on-site, per day: **305**
- Total hours worked: **438,361**
- Regional labor: **94%**

## Work Force By County

- Davidson
- Other (TN)
- Rutherford
- Other
- Wilson
- Coffee
- Sumner

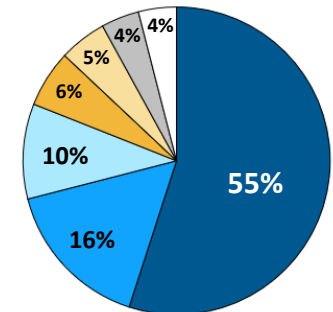

## Materials<sup>4</sup>

- % regional materials used: **95%**

<sup>1,4</sup> As of 12/1/2019

<sup>2</sup> As of 9/30/2019

<sup>3</sup> As of 12/6/2019
